



WORKS COMPLETED THIS WEEK

- Building A
 - Progressive backfill around building perimeter retaining walls
 - Column formwork to pour 2 upper floor suspended deck
 - Suspended slab
 – Formwork & Propping
 - Complete Steelfixing to Suspended Pour 1
 - Continue Services works to commence on pour 2 upper floor suspended deck
- Building B
 - Detailed excavation and Subsoil installation for SOG Pour 3
 - Mastatex installation to SOG Pour 3
 - Commence of membrane to SOG Pour 3
 - Installation of formwork for upper floor Pour 1
 - Civil works to Western Facade
 - Precast grouting and caulking to panels



WORKS PLANNED NEXT WEEK

- Building A
 - Pour Suspended Deck Raking Slab and Vertical Elements Pour 1 (South)
 - Strip edge boards to Raking Slab & Vertical Elements
 - Progressive backfill around building perimeter retaining walls
 - Column formwork to pour 2 upper floor suspended deck
 - Pour 2 Suspended Formwork & Propping
 - Services works to commence on pour 2 upper floor suspended deck
- Building B
 - Detailed excavation and Subsoil installation for SOG Pour 3
 - Mastatex installation to SOG Pour 3
 - Continuation of membrane to SOG Pour 3
 - Footings Pour 3
 - Installation of formwork for upper floor Pour 1
 - Civil works to Western Facade
 - Precast grouting and caulking to panels





Building A






Building B





Building A – Steel fixing to suspended deck



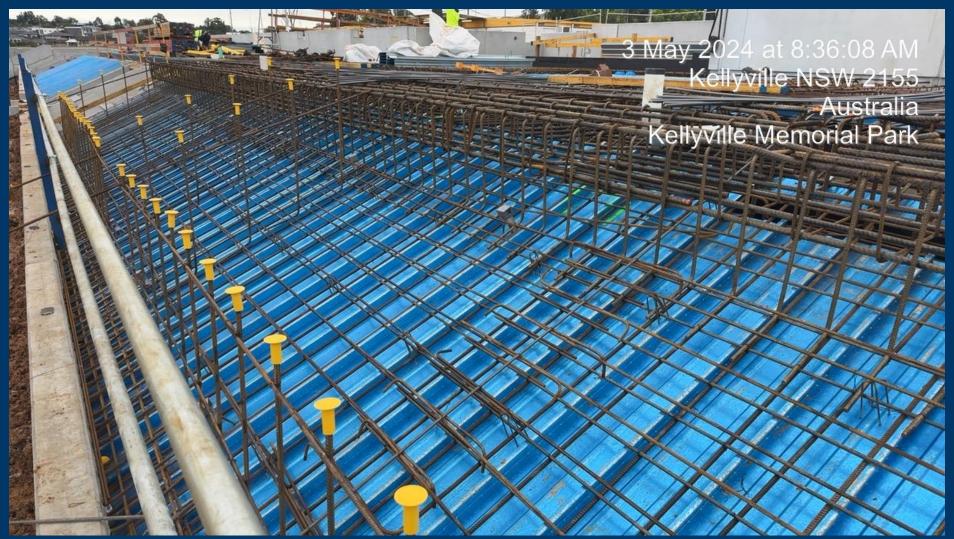

Building A – Rake soffit







Building A –Lower ground floor columns





Building B – Pool water testing









Building B – Upper floor formwork installation
