

KANE

Weekly Update

DATE: 26th of July 2024

MostynCopper



Waypoint 

WORKS COMPLETED THIS WEEK

Building A

- Continuation of High-level services installation
- Blockwork Installation (Lower Ground Suspended Deck Pour 2)
- In Slab Services Rough ins (Upper Floor SOG Pour 3)
- Pour Upper Floor Pour 3 (Footings)
- Pour Upstand Wall Footing (Upper Floor SOG Pour 4)
- Backfill footings & complete Raking Beam detailed excavation for Grandstand Plats
- Steel-fixing to raking beam
- Waterproofing to Raking Suspended Slab
- Detailed Excavation to SOG Pour 4

Building B

- Engineer inspection and sign-off to Structural Steel stage 1
- In-slab Services installation to Upper Floor Suspended Pour 3
- Installation of HD Bolts, Rebates and Set downs for (Upper Floor Suspended Pour 3)
- Concrete Pour to Upper Floor Suspended Pour 3
- Waterproofing to Lower Ground Floor Retaining Walls
- Commence Backfilling and Subsoil Drainage to Retaining Walls
- Commence Installation of Roof Safety Mesh (Drill Purlins)
- Continuation of Stud Framing to Lower Ground Floor
- Continuation of High-Level Services to Lower Ground Floor
- Rough-in Aquatic plumbing/pipe works

WORKS PLANNED NEXT WEEK

Building A

- Formwork Stripping to Upstand Walls (Upper Floor SOG Pour 4)
- Backfill & Detailed Excavation (Upper Floor SOG Pour 4)
- Commencement of Inground Drainage (Upper Floor SOG Pour 4)
- Installation of Spiral Duct to core holes (External West)
- Steel fixing to corner ledge for Precast Plats (External West)
- Formwork to corner ledge for Precast Plats (External West)
- Pour concrete to Raking Beams (External Works)
- Formwork stripping to Raking Beams (External Works)

Building B

- Close 1 side of walls (LGF Fit-out works area Pour 1 area)
- Continue Installation of Services within Walls all service trades (LGF Fit-out works Pour 2 area)
- Commencement of Roofing to North to Grid B.J
- Cut Extensions, Seal and Grout Post Tensioning
- Installation of Remaining Upper Precast Panels (Upper Floor Suspended area Pour 3)
- Grouting, Caulking and Welding (Upper Floor Suspended area Pour 3)

PROGRESS PHOTOS

25/07/2024 10:20:00



Building A

PROGRESS PHOTOS


25/07/2024 15:20:01



Building B

KANE

PROGRESS PHOTOS

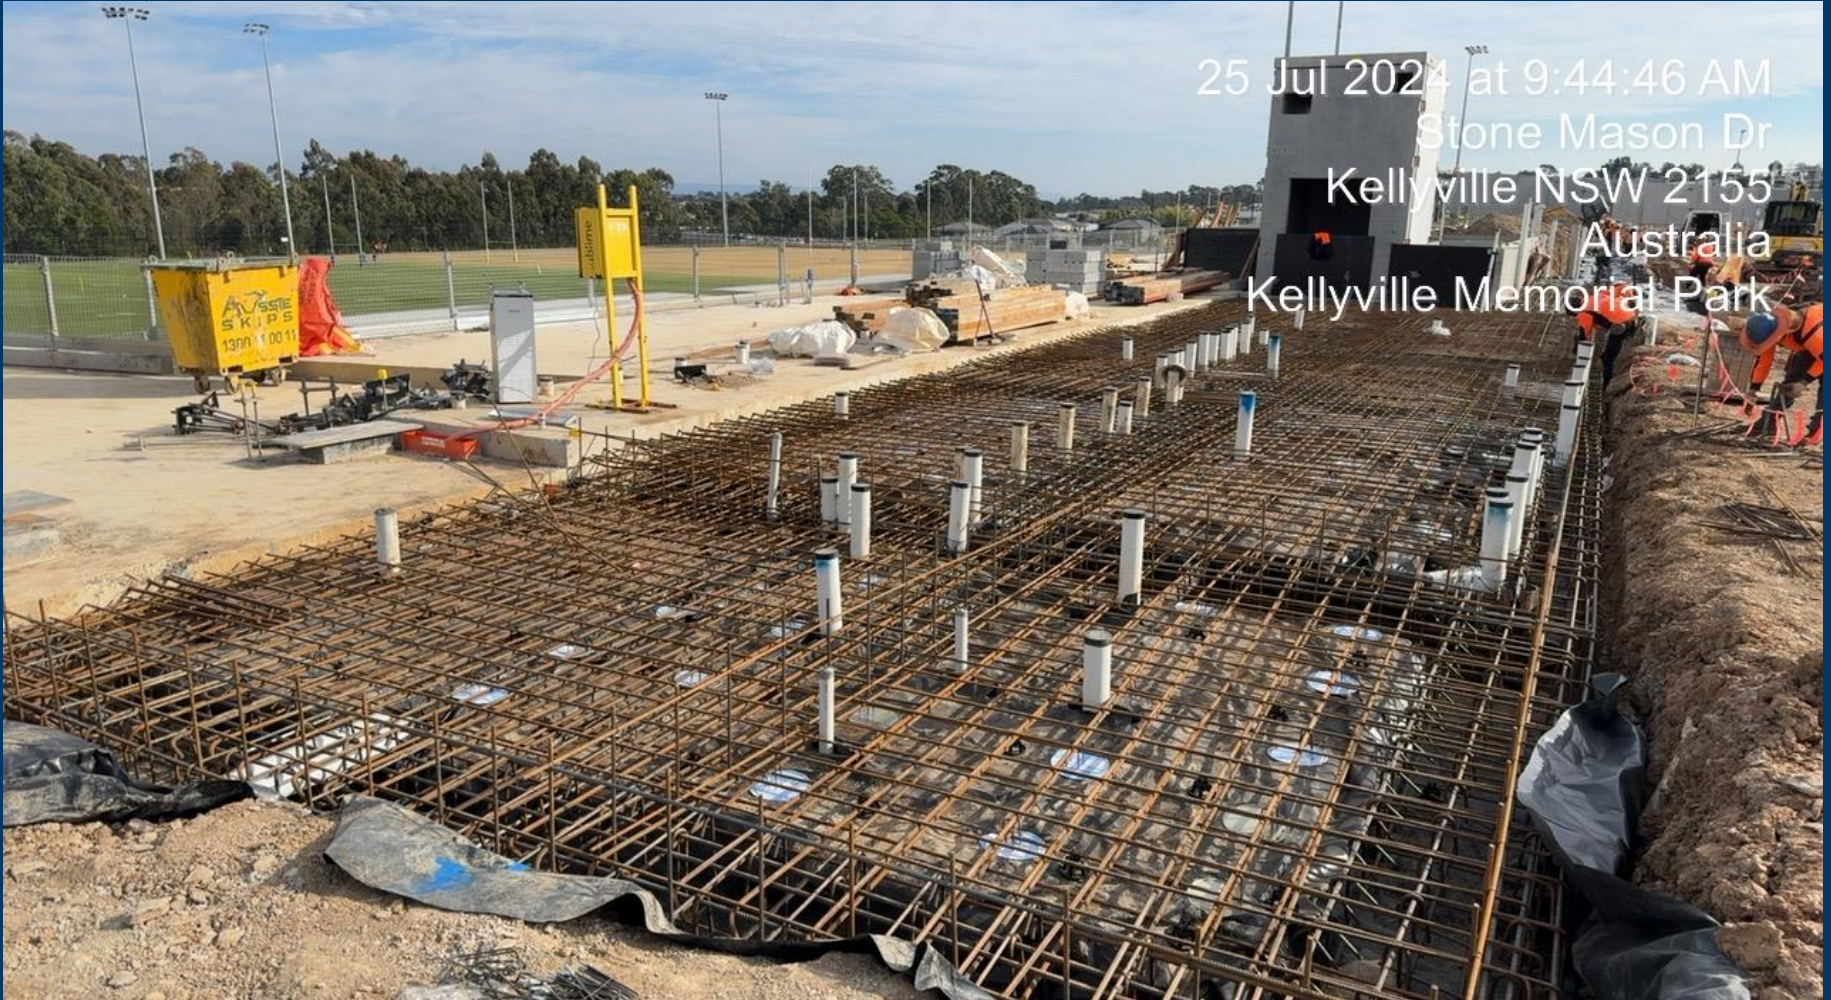

25 Jul 2024 at 9:44:46 AM
Stone Mason Dr
Kellyville NSW 2155
Australia
Kellyville Memorial Park

Building A – Upper Floor Pour 3 Steel fixing

KANE

PROGRESS PHOTOS

26 Jul 2024 at 8:23:08 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park



Building A – Upper Floor Pour 3 Footings

KANE

PROGRESS PHOTOS

26 Jul 2024 at 9:41:03 AM
311 Stone Mason Dr
Kellyville NSW 2155
Australia
Kellyville Memorial Park



Building A – Upper Floor Pour 3 Footings

PROGRESS PHOTOS

26 Jul 2024 at 8:27:57 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park



**Building A – Detailed Excavation External
West**

PROGRESS PHOTOS



25 Jul 2024 at 9:51:16 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park

**Building A – Blockwork installation Lower
Ground Floor**

KANE

PROGRESS PHOTOS

26 Jul 2024 at 8:33:04 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park



**Building A – Commencement of Services
Lower Ground Floor (Gym)**

KANE

PROGRESS PHOTOS




25 Jul 2024 at 9:58:06 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park

**Building B – Structural Steel Installation to
Upper Floor Pour 1 and Pour 2**

KANE

PROGRESS PHOTOS

25 Jul 2024 at 10:06:07 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park

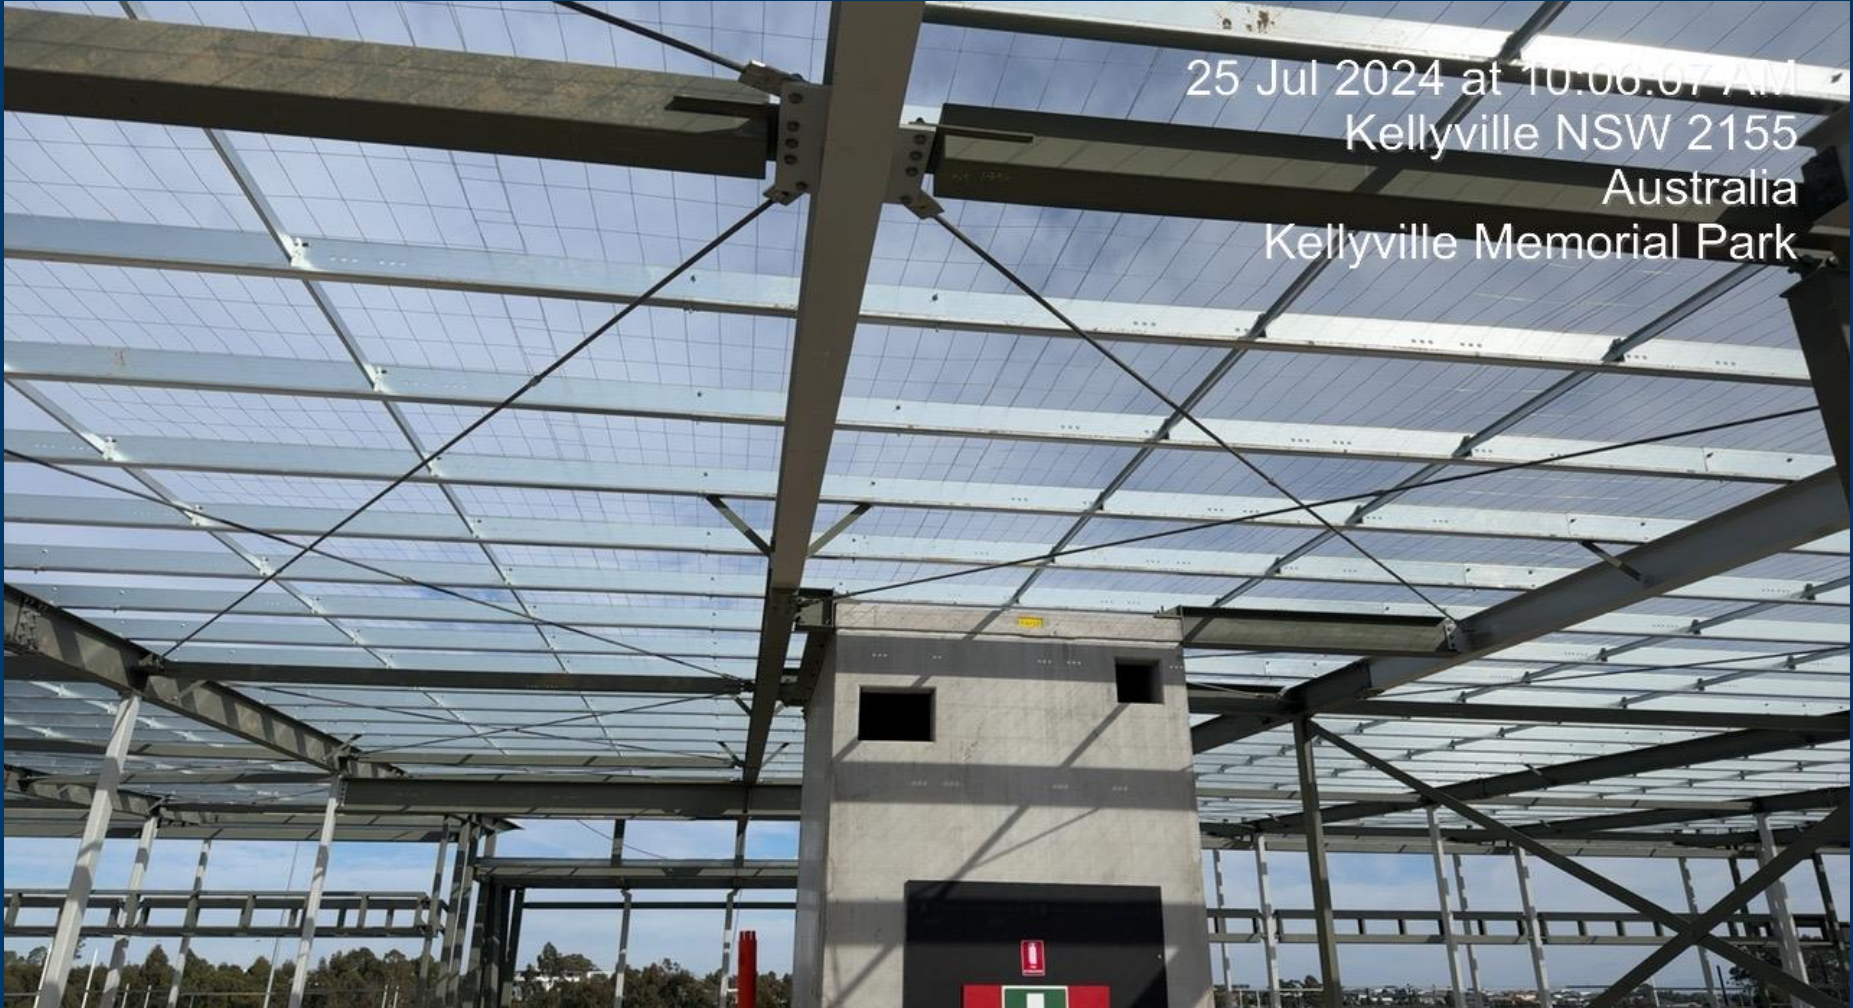

Building B – Installation of Roof Safety Mesh

PROGRESS PHOTOS

25 Jul 2024 at 9:59:19 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park



**Building B – Lower Ground Floor Services
Work Pour 2 area**

KANE

PROGRESS PHOTOS



24 Jul 2024 at 4:38:32 PM
Kellyville NSW 2155
Australia
Kellyville Memorial Park

Building B – Upper Floor Suspended Deck Pour 3
