

WORKS COMPLETED THIS WEEK



Building A

- First & Second Coat to Tunnel Walls
- Installation of Handrails (LGF Northern Tunnel)
- Installation of Doors & Fixed Panels (LGF Areas)
- Floor Preparation and Vinyl Installation (LGF Areas)
- Installation of Toilet Partitions (LGF)
- Installation of Joinery (LGF Areas)
- Services Fit-off (LGF Areas)
- Internal Sheeting, Setting and Sanding (Walls and Ceilings Coaches Box/ Media Box & Tenancy Area)
- External Framing to Kitchen (GF)
- Installation of Stadium Seating (South of Central Tunnel)

Building B

- Fit out of Finishes within Aquatic Pool
- Service Fit off to Ceilings & Walls (LGF Pour 1, GF Pour 1, LGF Pour 2, GF Pour 2)
- Joinery Installation (LGF Pour 1)
- Installation of Timber Doors & Glass Doors (LGF Pour 1)
- Paint 1st Coat to Ceilings (GF Pour 1)
- Waterproofing to Wet Area Floors (GF Wet Areas)
- Installation of Aluminium Door Frames (LGF Pour 3)
- Ceiling Sheeting, Setting and Sanding (LGF Pour 3)
- Ceiling Framing (GF Pour 3)

WORKS PLANNED NEXT WEEK



Building A

- Installation of Joinery & Joinery Fit off (LGF Areas)
- Low Level Service Fit off (LGF Areas)
- Floor Preparation & Vinyl Installation (LGF Areas)
- Set & Sand Ceilings (LGF Areas)
- Painting Ceilings (LGF Areas)
- Sheeting, Setting and Sanding Walls (Coaches Box/Media Boxes & Plant Room)
- High Level Services Rough in (Coaches & Media Boxes)
- Ceiling Framing (Coaches & Media Boxes)
- Face Brickwork Headers and Cladding (Tenancy Area)
- Installation of Plinths (External Plant & Refuse Area)
- External Framing, Sarking and Internal Framing (Kitchen Area)
- Skylight Installation (Upper Floor Roof)

Building B

- Fit out of Finishes within Aquatic Pool
- Installation of Ceiling Tiles (LGF Areas)
- Door Hardware Installation (LGF Areas)
- Floor Preparation & Vinyl/Carpet Installation (GF Pour 1 & GF Pour 2)
- Joinery Installation (LGF Pour 2, GF Pour 1)
- Installation of Glass Doors (GF Pour 1)
- Ceiling Sheeting, Setting and Sanding (LGF Pour 3)
- Waterproofing Work & Installation of Pedestal Pavers (GF Staff Balcony)
- Installation of Glass Balustrades (GF Club Balcony & Staff Balcony)





Peter Sterling Site Visit





Building A



PROGRESS PHOTOS 15/11/2024 10:50:00





Building A – Brickwork (Tenancy Area)





Building A – Sheeting External Walls (Tenancy Area)





Building A – Roofing Complete (Tenancy Area)





Building A – External Sheeting (Coaches & Media Boxes)





Building A – Window Installation (Coaches & Media Boxes)





Building A – Commencement of Framing (GF Pour 3)



PROGRESS PHOTOS Plov 2024 at 10:39:43 am Kallyville NSW 2155 Australia Kellyville Memorial Park


Building A – Grandstand Seating Installation






Building A – Grandstand Seating Installation (South)

KANE

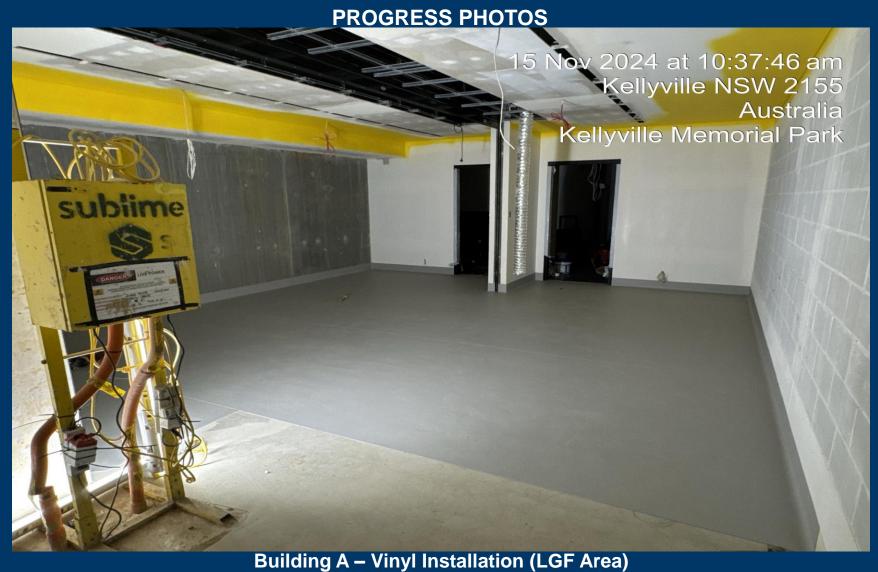

KANE

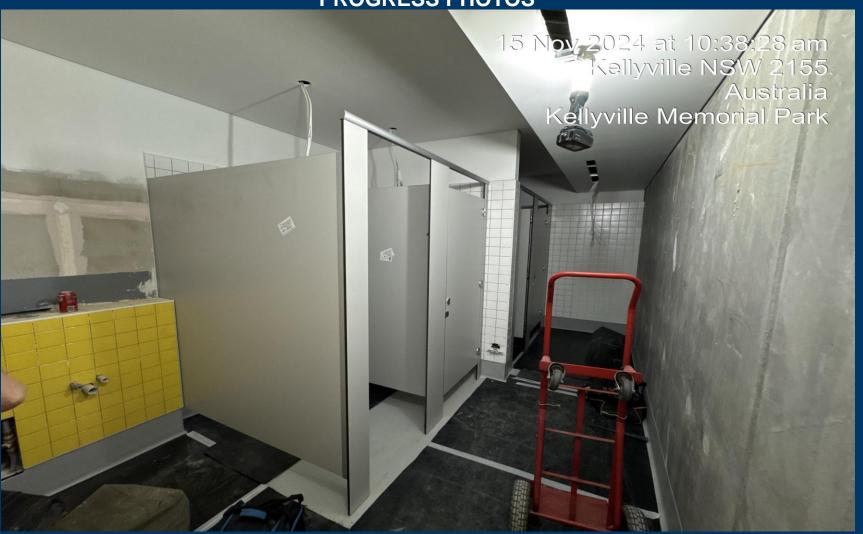

Building A – Installation of Toilet Partitions (LGF Area)





Building A – Installation of Toilet Partitions (LGF Area)





Steel Fixing to Meeting Place Circle





Steel Fixing to Meeting Place Stairs





Carpark Excavation





Building B – 1st Coat of Paint (GF Ceiling Pour 1)





Building B – 1st Coat of Paint (GF Ceiling Pour 1)






Building B – Joinery Installation (GF Pour 1)






Building B – Setting and Sanding Ceiling (GF Pour 2)



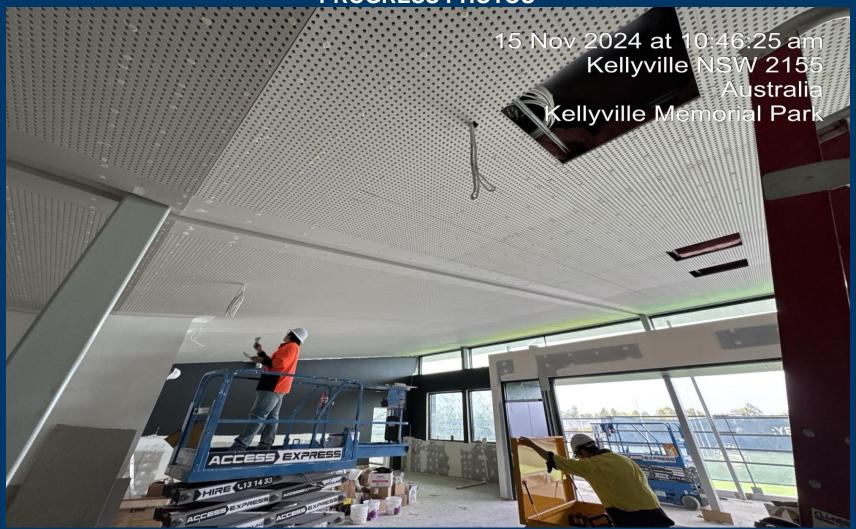


Building B – Setting and Sanding Ceiling (GF Pour 2)



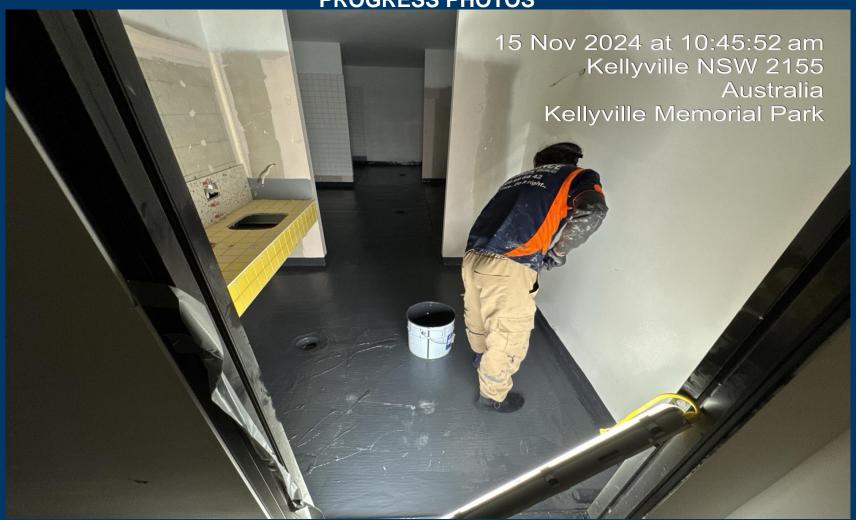

Building B – Waterproofing (GF Wet Areas)



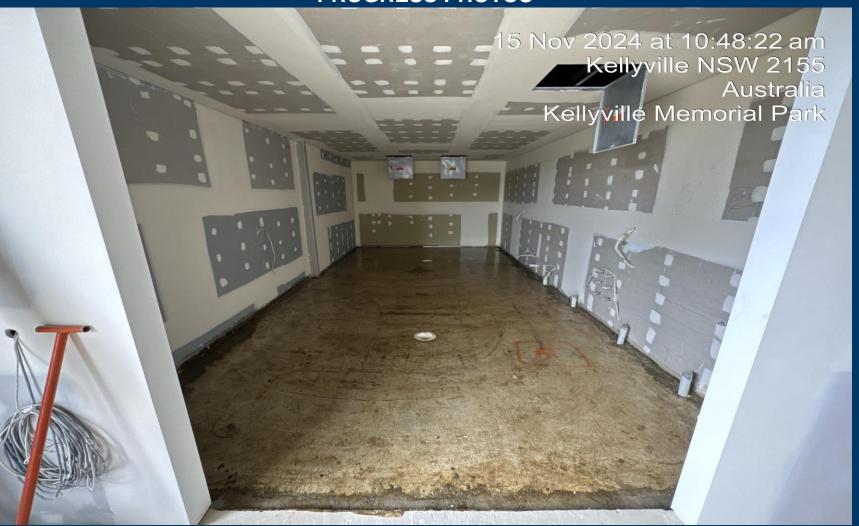

Building B – Floor Preparation (GF Pour 1)






Building B – Painting to Western Elevation





Building B – Door Hardware Installation (LGF Pour 1 Area)



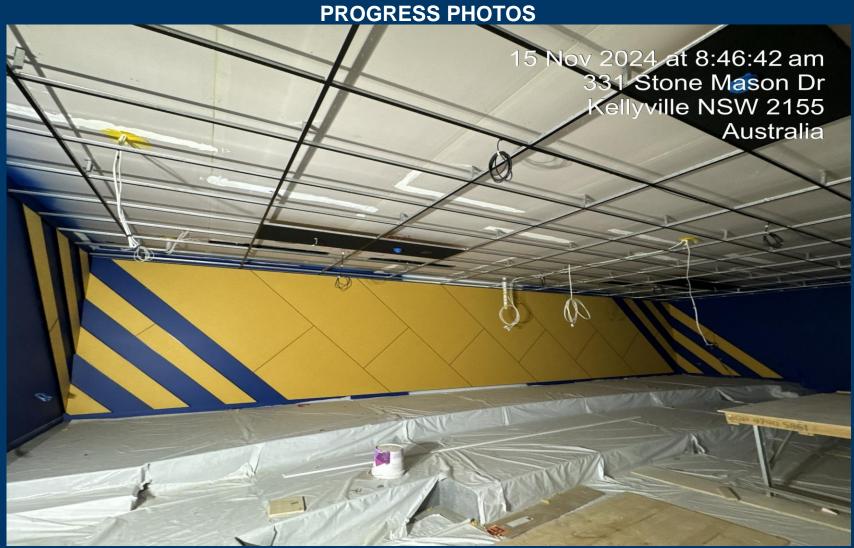

Building B – Acoustic Panels Installation (LGF Theatre Room)





Building B – Door Hardware Installation (LGF Pour 2 Area)





Building B – Joinery Installation (LGF Pour 2)
